


LEJ-640F

Pre-Installation Checklist



Imagine.

Dimensions and weight :

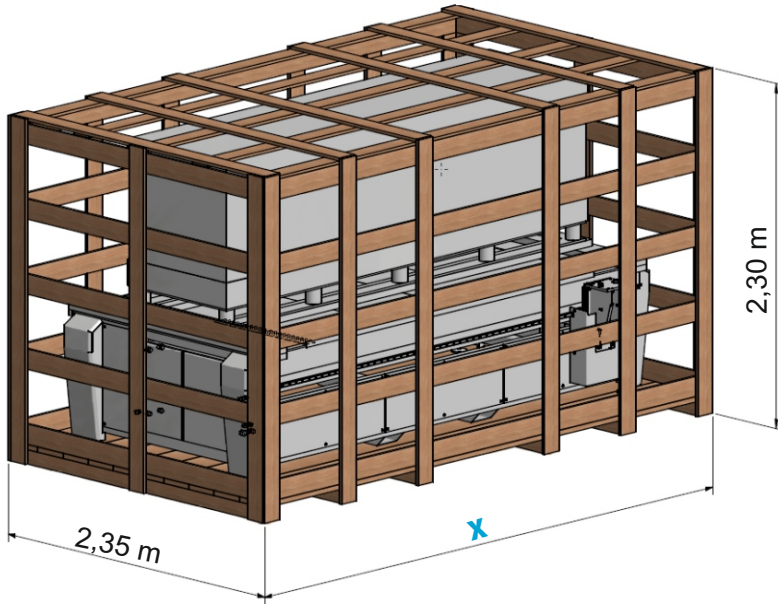

- **Depending on the model :**

TP-16-21	X	=	3,70 m	1200 kg
TP-16-25	X	=	4,10 m	1300 kg
TP-16-32	X	=	4,80 m	1500 kg

- **Necessary to unload and install :**

Forklift of 3,5 T with forks of 2m length

OK	Not OK

Customer Information

- **Customer Name** :
- **Contact Person** :
- **E-mail address** :
- **Installation address** :
.....
.....
- **Phone** :
- **Main Application** :
.....

• **Accessories to be installed :**

Frazer Antistatic Bar

Bofa Exhaust System

• **Requested installation date : (not fixed only as an indication)**

.../.../.....



Things to be checked onsite :

- **Minimum size necessary to bring the machine into the room, this also includes all doors and hallways to enter this room :**

2.30 m

OK	Not OK

- **Machine is delivered with a 3P + E 16A power plug :**



Customer needs to make sure to have the right power plug available



OK	Not OK


- **If the machine is delivered with a Bofa Exhaust filter or Frazer Antistatic bar the customer should also provide a power plug (220 V / 16 A) for each optional equipment.**

OK	Not OK

• **Compressed air connection and specification :**

**Machine is delivered with a quick connector of 10mm.
The customer should take care about of a 10 mm
tube and compressor.**

Connector on the Machine



Tube to be used



OK	Not OK

Pressure specification : between 4 and 7 bar

The customer agrees the above-mentioned topics have been checked and explained. The topics that have the status „Not OK“ should be clarified and arranged before installation. In case of missing things, Roland DG cannot be held responsible for any delay of installation or extra costs.

Signature Roland Partner / Employee

Signature Customer

